

CONFIDENTIAL



SKU Exit Tooling

Statement of Work

Version 1.0

September 21, 2026

This proposal is protected under the copyright laws of the United States and other countries as an unpublished work. This proposal contains information that is proprietary and confidential to Pfizer, which shall not be disclosed outside the recipient's company or duplicated, used or disclosed in whole or in part by the recipient for any purpose other than to evaluate this proposal. Any other use or disclosure in whole or in part of this information without the express written permission of Pfizer is prohibited.

Table of Contents

1	STATEMENT OF WORK	3
2	PFIZER PROJECT CHARTER	4
3	DETAILED SOLUTION	5
3.1	Solution Overview	5
3.2	Project Oversight	5
3.3	Solution Approach	5
3.4	Project Resources	5
3.5	Project Schedule with Milestones	6
3.6	Project Deliverables	6
3.7	Risks	6
3.8	Assumptions	6
4	COMMUNICATION PLAN	7
5	PERFORMANCE MEASUREMENT AND REPORTING	8
6	CHANGE CONTROL PROCEDURE	8
6.1	Change Control Process Flow	8
6.2	Change Control Process	8
7	ACCEPTANCE	9
8	PROJECT COSTS	9
8.1	Cost Model (select one)	9
8.2	Project Costs	9
8.3	Incentives/Penalties	10
8.4	Expenses	10
9	PAYMENT SCHEDULE AND PROCEDURES	10
10	TERMINATION	10
11	TRANSITION ASSISTANCE	11
12	SIGNATURE	12

1. STATEMENT OF WORK

This Statement of Work (“SOW”) is made and entered into as of September 21, 2026 (“Effective Date”), by and between Toptal, LLC (together with its subsidiaries and Affiliates “Supplier” or sometimes “Provider” or “Vendor”), having its principal place of business at 2810 N. Church St., #36879, Wilmington, DE 19802-4447 and Pfizer Inc (together with its subsidiaries and Affiliates “PFIZER”), having its principal place of business at 66 Hudson Boulevard East, New York, New York 10001.

WHEREAS

This Statement of Work is entered into pursuant to the Pfizer Inc – Toptal Services Agreement dated 11/16/2018, between Pfizer Inc. and Toptal, LLC, as amended by Amendment No. 1 to Services Agreement dated 11/8/2021 and Amendment No. 2 to Services Agreement dated 9/26/2024, relating to the provision by Toptal, LLC of certain services as defined therein (the “Master Agreement”). The terms and conditions of the Master Agreement govern this Statement of Work in respect of the following Services with the following additional provisions applying:

Project Name:	SKU Exit Tooling
Supplier Name:	Toptal, LLC
Address:	2810 N. Church St., #36879
	Wilmington, DE 19802-4447
Contact (Name):	Anoop George
Phone:	973-204-4822
E-mail:	Anoop.George@toptal.com

2. PFIZER PROJECT CHARTER

Business Sponsor: Mark Dannatt

Pfizer Project Manager: Daniel Itriago

Scope of the Project:

Pfizer's Commercial Portfolio Management (CPM) team manages SKU discontinuation requests through the Train Track tool, while a separate, Regulatory-owned local tool handles locally-initiated requests; the consolidated pipeline comprises approximately 1,240–1,340 active records across both systems. This engagement stabilizes the existing Train Track application and evaluates, then, contingent on approval, builds a consolidated, integrated, platform. The engagement is structured as two sequential workstreams: Phase 1 (Discovery + Stabilization) and Phase 2 (Rebuild).

Project Goals and Objectives:

The goal of this engagement is to help Pfizer stabilize the existing Train Track system while supporting the designing and building of a more capable, connected platform

Phase 1 Objectives (goals):

- Support an interim fix (patch) for the recurring defects limiting Train Track's usefulness today by helping repair: bulk upload, failing notifications, and unreliable REG21 sync.
- Once the interim fix is in place, help keep Train Track operational for its ~15 active users through the end of Phase 1, with minimal disruption to the CPM-owned process.
- Phase 1 gap assessment to help establish technical ownership of a system Pfizer currently manages ad hoc, with no dedicated internal development team.
- Support the creation of a rebuild approach and a detailed Phase 2 Build Plan for Pfizer's approval.

Phase 2 Objectives (goals):

- Support the execution of the approved Phase 2 Build Plan
- Help establish a consolidated system of record spanning the CPM-managed Train Track pipeline and the Regulatory-owned local tool.
- Support scaling the platform for an increased number of requestors and users, with unlicensed front-end access for request submission and status checking by Pfizer employees.
- Assist with integrations defined as part of the scope at the end of Phase 1.
- support resolution of the change requests identified in the Process & Steps Review as part of Phase 1 discovery outcomes.
- support realignment of Power BI reporting across the Train Track views

- Draft documentation, training materials, and UAT coordination, and to assist with cutover to production by the end of the SOW term, followed by a defined hypercare period.

NOTE: Pfizer's approval of the Phase 2 Build Plan impacts all Phase 2 work and any material deviations from the approved Phase 2 Build Plan may require an adjustment to this SOW and will be handled in accordance with the Change Control Procedures outlined in Section 6 of this SOW.

Pfizer seeks talent to provide support in the following areas:

- Power Platform solution architecture and hands-on development (Dataverse schema, security/access model, Power Apps back-end views, Power Pages front-end portal) to stabilize Train Track.
- Support business analysis to drive the gap assessment, stakeholder interviews, and rebuild approach.
- Assist with QA/test engineering.
- Project management support.

Project Start Date: On or about the Effective Date, but not until a purchase order has been established. If the Project Start Date is delayed, the End Date may require adjustment.

Timeframe for Completion: The overall scope of the project will be for twenty-two (22) weeks from the Effective Date. The SOW termination date will be on or about February 20, 2027.

Deliverables and expected business outcomes:

Pfizer's expected business outcome in connection with this SOW is for the talent to provide support to Pfizer's SKU Exit Tooling project to help stabilize the existing Train Track platform, and then, subject to Pfizer's approval of the Phase 2 Build Plan, to support the execution of the Phase 2 Build Plan to help build a consolidated and integrated platform.

- Support an interim fix to repair the three broken functions: bulk upload, segment-change/SupplyIQ upload email automation, and Stewardship T5/T6 retrieval.
- Support the creation of the Gap Assessment Report covering the current Power Apps implementation.
- Help provide a recommendation report with a rebuild-approach.
- Support the development of a detailed staffed Phase 2 Build Plan (staffing, schedule, milestones).

Phase 2 (subject to Pfizer's approval of the Phase 2 Build Plan):

- Support the execution of the approved Phase 2 Build Plan, which may include:
 - Supporting the creation of a published solution design covering the consolidated screen flow, workflow and business logic, and integration architecture.

- Support building and testing the core platform and consolidation logic on the Microsoft Power Platform, including the Dataverse schema and security roles, Entra ID access model, Power Pages portal, and Power Apps back-end views for CPM.
- Help resolve the change requests identified in the Process & Steps Review, such as bulk upload, notifications, REG21 status automation, rejected-SKU handling, and archiving.
- Support realignment of the Power BI report to the resulting data model across the Train Track views.
- Support the creation of user, administrator, and technical documentation and training materials, and assist Pfizer with UAT coordination.
- Assist with cutover preparation and production deployment, and support the transition to the support model selected by Pfizer.

NOTE: The Phase 2 items above may be changed in the final Phase 2 Build Plan approved by Pfizer, and where the approved Phase 2 Build Plan will be materially different from the items described above, the project scope may require adjustment.

3. DETAILED SOLUTION

3.1. Solution Overview

Provider-sourced talent will provide services for Pfizer's SKU Exit Tooling project to support stabilization fixes for broken production functions, discovery, and a gap assessment to help identify the optimal approach for Phase 2.

3.2. Project Oversight

Pfizer Project Manager will have oversight of the project with collaboration, support, and assistance from VENDOR and VENDOR assigned delivery manager. The Toptal-sourced talent will work pursuant to instructions, guidance and direction of the Pfizer Project Manager. Vendor's assigned Delivery Manager will help with sprint execution, resource allocation, and regular status reporting.

Pfizer will assign a Project Manager or Product Owner responsible for overarching project governance. The Pfizer Project Manager will facilitate access to required internal systems, data, and subject matter experts, and will be responsible for reviewing, testing, and approving all milestones and final deliverables. Project oversight will be maintained through regular sprint ceremonies, progress reports, and defined decision gates.

3.3. Solution Approach

Under this SOW, the resources sourced to Pfizer by Supplier will assist Pfizer with developing

Project Deliverables.

3.4. Project Resources

Company	Name	Title/role	Reports to; name/title	Key Personnel (Y/N)	On/Off shore	% assigned to project
Toptal-sourced talent	TBD	Project Manager	Pfizer Project Manager	TBD [CONFIRM]	Off	50%
Toptal-sourced talent	TBD	Business Analyst	Pfizer Project Manager	TBD [CONFIRM]	Off	50%
Toptal-sourced talent	TBD	Power Platform Solutions Architect	Pfizer Project Manager	TBD [CONFIRM]	On	75%
Toptal-sourced talent	TBD	QA / Test Engineer	Pfizer Project Manager	TBD [CONFIRM]	Off	37.5%
Toptal-sourced talent	TBD	Power Platform Developer (Backend)	Pfizer Project Manager	TBD [CONFIRM]	Off	100%
Toptal-sourced talent	TBD	Integration Engineer (x2)	Pfizer Project Manager	TBD [CONFIRM]	Off	100%
Toptal-sourced talent	TBD	Frontend Developer	Pfizer Project Manager	TBD [CONFIRM]	Off	100%

3.5. Project Schedule with Milestones

To be set by the direction of the Pfizer Project Manager.

Desired Milestone based on a Start Date of September 21, 2026:

- Milestone 1.1 – Support completion of Gap Assessment report including findings from stakeholder interviews, technical review, hands-on defect reproduction and evidence gathering, and a Regulatory data-profiling spike for consolidation logic and the provision of a summary to the CPM Product Owner for review (which is currently expected to occur on or around October 9, 2026). Desired result: Gap Assessment report.
- Milestone 1.2 – Help provide a recommendation report with a rebuild approach and a draft phase 2 build plan describing staffing and desired schedule/milestones (which is currently expected to occur on or around October 9, 2026). Desired result: Implementation plan.
- Milestone 1.3 – Pfizer shares a decision regarding the Phase 2 build plan and confirms that it would like to proceed (which is currently expected to occur on or around October 16, 2026). If Pfizer needs to pause the engagement for internal process compliance, the milestone dates and End Date may require adjustment.
- Milestone 2.1 – Support stabilization fixes and live deployment of the platform that is verified with CPM, and active Train Track platform (which is currently expected to occur on or around October 16, 2026). Desired result: Current application up and running with existing functionalities.
- Milestone 3.1 – Support the completion of the solution design, screen flow, and wireframe sketches based on the Phase 1 gap assessment and prioritized change list. Desired result: Design documents listed above.
- Milestone 3.2 – Support the build and testing of the core platform and consolidation (which is currently expected to occur on or around December 18, 2026). Desired result: Project execution documents with implementation plan, progress reports, and test cases outlined.
- Milestone 3.3 – Support the Power BI report realignment, implementation, documentation, and training materials with UAT coordination (which is currently expected to occur on or around February 05, 2027). Desired result: User interface documents with implementation plan, progress reports, and test cases outlined.
- Milestone 3.4 – Assist with the cutover preparation, documentation, and production deployment to support the platform live in production with a support model selected and operational (which is currently expected to occur on or around February 12, 2027). Desired result: Go-live and cutover plans, knowledge transfer, and general user documentation.

NOTE: Milestones described above are based on information currently available, and may be adjusted based on the outcomes of the phase 1 discovery and Pfizer approved phase 2 build plan, which may require adjustments to the above dates. Any updates to the milestones, dates, or project scope will be handled in accordance with the Change Control Procedures outlined in Section 6 of this SOW.

3.6. Project Deliverables

To be set by the Pfizer Project Manager, consistent with above project schedule/milestones.

3.7. Risks

This Statement of Work was prepared, and this project will be executed, under the following assumption(s):

Owner (Pfizer or VENDOR)	Risk Event	Potential Impact Description	Probability of occurrence (H/M/L)	Impact of occurrence (H/M/L)	Mitigation Plan	Overall Risk Profile (H/M/L)
Pfizer	Deliverables not well defined	Deliverables are incorrect, resulting in rework/delay	L	H	Confirm understanding prior to each phase	L
Pfizer	Business SME's unavailable for requirement definition	Requirements not defined in a timely manner resulting in delay	M	H	Identify business SME's and confirm time commitments with Steering team	L
VENDOR	Unqualified resources assigned to the project	Deliverables delayed, missed, or of low quality	L	H	Change the resources	L
VENDOR	Site resources not available to enable completion of deliverables	Deliverables are incomplete or of low quality	L	H	Escalate to Pfizer project manager for resolution	M

3.8. Assumptions

This Statement of Work was prepared, and this project will be executed, under the following assumption(s):

Company	Assumption description	Relevance
Pfizer	Will provide a Project Manager responsible for this project and provide overall direction to VENDOR personnel with collaboration, support, and assistance from VENDOR and VENDOR assigned delivery manager.	Entire Project
Pfizer	Pfizer will provide appropriate subject matter experts (business and technical) to answer questions and provide additional information within the work plan schedule. Delays that affect the planned timeline will be assessed for time and cost implications and may require a Project Change Request (to be approved by Pfizer) and additional funding billable to Pfizer.	Entire Project
Pfizer	The timeline assumes Pfizer will supply, in a timely manner, appropriate personnel for informal consultation (e.g., phone, email) and formal review (e.g., review meetings, test sessions) as needed.	Entire Project
Pfizer	Delays from Pfizer due to missed deadline commitments, cancelled meetings, delayed receipt of required information, or the result of an unstable working environment that affect the planned timeline will be assessed for time and cost implications and may require a Project Change Request (to be approved by Pfizer) and additional funding billable to Pfizer.	Entire Project
Pfizer	Pfizer will identify and provide to Supplier any/all standards and guidelines within project scope (e.g., documentation standards, operating procedures, etc.) that must be followed by VENDOR in the course of this project. Any standards or guidelines (technical or business-related) identified or provided to Supplier after the start of the project may require a Project Change Request (to be approved by Pfizer) and additional funding billable to Pfizer.	Entire Project
Pfizer	Will provide office space, computer hardware, software, system connectivity, desks, telephones, copy and fax facilities, supplies and conference rooms for VENDOR consultants assigned to this project at Pfizer's facilities, as required.	Entire Project
VENDOR	Main work location for this project to be remote	Entire Project
Pfizer	Pfizer will provide network logon ID(s) and system access	Entire

Company	Assumption description	Relevance
	as necessary to complete the project.	Project
Pfizer	Delays due to Network/Hardware, Operating Systems difficulties, and/or delays with Application Support at Pfizer that cause the project to be extended will be assessed for time and cost implications and may require a Project Change Request (to be approved by Pfizer) and additional funding billable to Pfizer.	Entire Project
VENDOR	VENDOR sourced Talent will transition finished work product to Pfizer project team members and production support team prior to production implementation, if required	Entire Project
Pfizer/ VENDOR	VENDOR will source the resources to Pfizer and Pfizer will be responsible for determining the resource requirements and assignments for this project in consultation with VENDOR.	Entire Project
Pfizer / VENDOR	Pfizer will be responsible for providing accurate and timely feedback on all issues. VENDOR will document all decisions made during this project, and all such documentation will be forwarded to Pfizer.	Entire Project
Pfizer / VENDOR	VENDOR will provide support for the hours documented in this SOW. If the project is not completed within the amount of hours and End Date, VENDOR will create a Change Control to complete the work or Pfizer may elect to complete work internally.	Entire Project

4. COMMUNICATIONS PLAN

Pfizer and VENDOR will agree to the communications plan and any adjustments to same required throughout the project. The communications plan will be managed by the Pfizer Project Manager. VENDOR resources can report any issues to Project Manager.

-

5. PERFORMANCE MEASUREMENT


Performance measurement and reporting metrics will be tracked and managed by the Pfizer Project Manager in consultation with VENDOR assigned delivery manager. Daily standups, sprint planning, backlog grooming, sprint review/demo, retrospective.

6. CHANGE CONTROL PROCEDURE

6.1. Change Control Process Flow



v1 SOW Change Control Process

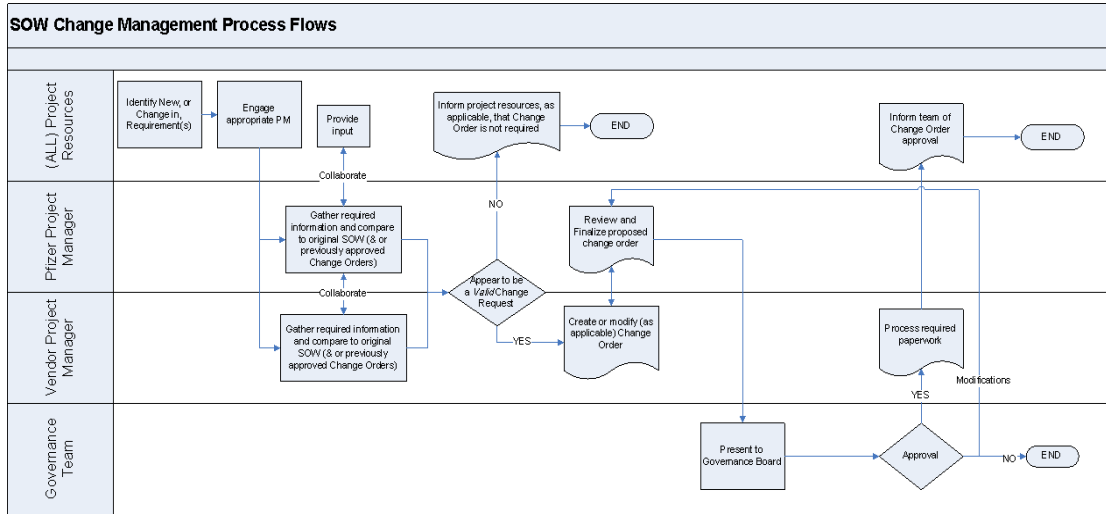

6.2. Change Control Process

In accordance with the overarching agreement identified in the Master Agreement and section 1 *Statement of Work*; the following change management procedure applies to this SOW.

1. *Project Resource(s)* may identify new or change in requirements and escalate to the respective *Project Manager*
2. *Supplier and Pfizer Project Managers* shall work together to gather required information to determine if *Change Order* is required
3. Project Managers shall determine if *Change Order* is required
 - a. If no, Project Resources will be informed, and the change management process ends
 - b. If yes, *Supplier Project Manager* will facilitate the creation of the *Change Order* and provide it to the Pfizer Project Manager
4. *Pfizer Project Manager* will review the proposed *Change Order*, with appropriate Pfizer resources, for content and completeness, and accuracy
 - If proposed *Change Order* requires changes; Pfizer Project Manager and Supplier Project Manager will collaborate to incorporate necessary modifications
5. *Pfizer Project Manager* will present proposed *Change Order* to the *Project*

Governance Team for final approval

- Additional revisions may be required; if so, go back to Step 4 and work with *Supplier Project Manager* to have modifications made, as applicable
- 6. If approved, the appropriate *Pfizer Manager* and *Provider Project Manager* will both sign *Change Order*
- 7. *Pfizer Project Manager* will inform the *Supplier Project Manager* and process required paperwork
- 8. *Pfizer Project Manager* and *Supplier Project Manager* will perform administrative project tasks, associated to the project and inform the *Project Resources* accordingly
- 9. End of *Change Order*

7. ACCEPTANCE

Project Acceptance is the Final Deliverable of this SOW.

VENDOR will have fulfilled its obligations under this SOW when any one of the following first occurs:

- a. Pfizer cancels the project in accordance with the provisions of the Master Agreement between Pfizer and VENDOR.
- b. VENDOR-sourced resources provide the deliverables described in Section 8.2 within the number of effort hours of service specified in Section 8.2, including any approved Change Control Forms.

8. PROJECT COSTS

8.1. Cost Model (select one)

- ☐ Fixed Price
- ☐ Time and Materials
- ☒ Time and Materials (Not to exceed)

8.2. Project Costs



v1 SOW Cost
Estimate Template.xls

Professional Services							
Universal Job Title	Talent name	Resource Level	Location	# of FTE	Rate/Hr.	# of hours	Estimated cost
Project Manager	TBD	Senior	Offshore	1.00	85.00	440.0	37,400.00
Business Analyst	TBD	Senior	Offshore	1.00	85.00	80.0	6,800.00
Power Platform Developer	TBD	Senior	Offshore	1.00	85.00	480.0	40,800.00
Power Platform Solutions Architect	TBD	Senior	Offshore	1.00	85.00	280.0	23,800.00
Quality Assurance Engineer	TBD	Senior	Offshore	1.00	85.00	280.0	23,800.00
Integration Engineer	TBD	Senior	Offshore	2.00	85.00	420.0	35,700.00
Frontend Developer	TBD	Senior	Offshore	1.00	85.00	320.0	27,200.00
Delivery Manager - Investment	Carolina Gurvich	Senior	Offshore	1.00	0.00	0.0	(20,000.00)
Client Partner	Carmelo Vignoli	Senior	Offshore	1.00	0.00	0.0	0.00
Principal Client Partner, Strategic Accounts	Anoop George	Senior	Offshore	1.00	0.00	0.0	0.00
Total				11.00		2300.0	175,500.00
Other							
Category	Description						Cost
Training Materials							
Travel and Meetings							
Software Licenses							
Software Maintenance							
Hardware							
Hardware Maintenance							
Content and Data Purchases							
Other Expenses							
<<Insert>>							
<<Insert>>							
<<Insert>>							
<<Insert>>							
						Subtotal	\$0.00
						Total	\$175,500.00

Toptal is offering the Delivery Manager, Client Partner, and Principal Client Partner, Strategic Accounts (collectively, “Support Team”) identified in this SOW as a courtesy and at Pfizer’s request to help enable Pfizer’s success with its project.

Pfizer acknowledges that the Support Team are not members of Toptal’s talent network and have not completed Toptal’s screening process and that the provisions associated with Toptal-sourced talent in the Master Agreement will not apply. Further, Toptal has agreed to waive any fees related to the work of the Support Team identified in this SOW that would have otherwise been payable by Pfizer.

8.3. Incentives/Penalties

There are no formal incentives or penalties associated with this scope of work.

8.4. Expenses

- The Master Agreement referenced and Section 1 *Statement of Work* in this SOW, identifies the overarching agreement in which to refer to regarding expenses.
- Expenses are to be reviewed and approved prior to invoicing.

9. PAYMENT SCHEDULE & PROCEDURES

The Provider will invoice monthly for the ongoing time and materials deliveries of its resources.

Payment terms are net 90 upon receipt invoice.

It is the responsibility of the Supplier Project Manager to identify all resources that will be required to access Pfizer facilities and or systems in compliance with required Pfizer lead times to ensure Supplier resources can access required facilities and systems upon their arrival. Pfizer will not reimburse the Supplier for idle resources if the delay is due to poor planning and or lack of communication by the Supplier Project Manager.

10. TERMINATION

This SOW shall be effective on the Effective Date hereof and, unless terminated sooner as provided herein, shall remain in effect through completion of the agreement as indicated by the End Date in Section 2 and subject to determination that such Work conforms with the requirement and specifications provided herein.

PFIZER may terminate this SOW upon five (5) days prior written notice to the Supplier.

11. TRANSITION ASSISTANCE

Pfizer may choose to transition all or part of the services described in this SOW to another supplier or internally within Pfizer upon five (5) days notice to the Supplier. In the event that Pfizer provides such notice to the Supplier, the Supplier shall fully cooperate with Pfizer and any such alternate supplier throughout the transition process as requested by Pfizer.

12. SIGNATURE

IN WITNESS WHEREOF, Provider and Pfizer have caused this Statement of Work to be duly executed and delivered as of the date first written above.

PFIZER INC

TOPTAL, LLC

Signed by:

B6F56CB132DE4EC...
Signature

Signed by:

749293F05EDE436...
Signature

Mark Dannatt

Print Name

Carlos Aguirre

Print Name

VP, Commercial Portfolio Management

Title

CFO

Title

September 18, 2026 | 5:14 AM PDT

Date

September 17, 2026 | 12:08 PM PDT

Date

Certificate Of Completion

Envelope Id: E9AE982A-B6B7-87EB-8330-F5850DAC707D

Status: Completed

Subject: Pfizer SOW 350 - MD

Source Envelope:

Document Pages: 17

Signatures: 2

Envelope Originator:

Certificate Pages: 5

Initials: 0

Rosali Naranjo

AutoNav: Enabled

2810 N. Church St #36879

Envelopeld Stamping: Enabled

Wilmington, DE 19802

Time Zone: (UTC-08:00) Pacific Time (US & Canada)

rosali.naranjo@toptal.com

IP Address: 2803:9800:9998:

Record Tracking

Status: Original

Holder: Rosali Naranjo

Location: DocuSign

9/17/2026 11:54:59 AM

rosali.naranjo@toptal.com

Signer Events

Carlos Aguirre

carlos.aguirre@toptal.com

CFO

Toptal, LLC

Security Level: Email, Account Authentication
(None)

Signature

Signed by:

Carlos Aguirre
749293F05EDE436...

Signature Adoption: Pre-selected Style
Using IP Address: 98.118.100.183

Timestamp

Sent: 9/17/2026 11:59:47 AM

Viewed: 9/17/2026 12:08:01 PM

Signed: 9/17/2026 12:08:11 PM

Electronic Record and Signature Disclosure:

Not Offered via Docusign

Mark Dannatt

Mark.Dannatt@pfizer.com

VP, Commercial Portfolio Management

Security Level: Email, Account Authentication
(None)

Signed by:

Mark Dannatt
B6F56CB132DE4EC...

Signature Adoption: Pre-selected Style
Using IP Address: 168.224.160.14

Sent: 9/17/2026 11:59:48 AM

Viewed: 9/18/2026 5:12:41 AM

Signed: 9/18/2026 5:14:00 AM

Electronic Record and Signature Disclosure:

Accepted: 9/18/2026 5:12:41 AM

ID: d056f9a3-c176-4e94-9a21-6847112e78c3

In Person Signer Events

Signature

Timestamp

Editor Delivery Events

Status

Timestamp

Agent Delivery Events

Status

Timestamp

Intermediary Delivery Events

Status

Timestamp

Certified Delivery Events

Status

Timestamp

Carbon Copy Events

Status

Timestamp

Carmelo Vignoli

carmelo.vignoli@toptal.com

Security Level: Email, Account Authentication
(None)

COPIED

Sent: 9/17/2026 11:59:48 AM

Electronic Record and Signature Disclosure:

Accepted: 6/16/2026 9:17:23 AM

ID: 5de55da2-75e4-4772-aeab-4f9b3332f310

Carbon Copy Events	Status	Timestamp
Carolina Gurvich carolina.gurvich@toptal.com Security Level: Email, Account Authentication (None) Electronic Record and Signature Disclosure: Not Offered via DocuSign	COPIED	Sent: 9/17/2026 11:59:49 AM Viewed: 9/18/2026 5:18:13 AM

Witness Events	Signature	Timestamp
----------------	-----------	-----------

Notary Events	Signature	Timestamp
---------------	-----------	-----------

Envelope Summary Events	Status	Timestamps
Envelope Sent	Hashed/Encrypted	9/17/2026 11:59:49 AM
Certified Delivered	Security Checked	9/18/2026 5:12:41 AM
Signing Complete	Security Checked	9/18/2026 5:14:00 AM
Completed	Security Checked	9/18/2026 5:14:00 AM

Payment Events	Status	Timestamps
----------------	--------	------------

Electronic Record and Signature Disclosure
--

CONSUMER DISCLOSURE

From time to time, Toptal, LLC (we, us or Company) may be required by law to provide to you certain written notices or disclosures. Described below are the terms and conditions for providing to you such notices and disclosures electronically through the DocuSign, Inc. (DocuSign) electronic signing system. Please read the information below carefully and thoroughly, and if you can access this information electronically to your satisfaction and agree to these terms and conditions, please confirm your agreement by clicking the 'I agree' button at the bottom of this document.

Getting paper copies

At any time, you may request from us a paper copy of any record provided or made available electronically to you by us. You will have the ability to download and print documents we send to you through the DocuSign system during and immediately after signing session and, if you elect to create a DocuSign signer account, you may access them for a limited period of time (usually 30 days) after such documents are first sent to you. After such time, if you wish for us to send you paper copies of any such documents from our office to you, you will be charged a \$0.00 per-page fee. You may request delivery of such paper copies from us by following the procedure described below.

Withdrawing your consent

If you decide to receive notices and disclosures from us electronically, you may at any time change your mind and tell us that thereafter you want to receive required notices and disclosures only in paper format. How you must inform us of your decision to receive future notices and disclosure in paper format and withdraw your consent to receive notices and disclosures electronically is described below.

Consequences of changing your mind

If you elect to receive required notices and disclosures only in paper format, it will slow the speed at which we can complete certain steps in transactions with you and delivering services to you because we will need first to send the required notices or disclosures to you in paper format, and then wait until we receive back from you your acknowledgment of your receipt of such paper notices or disclosures. To indicate to us that you are changing your mind, you must withdraw your consent using the DocuSign 'Withdraw Consent' form on the signing page of a DocuSign envelope instead of signing it. This will indicate to us that you have withdrawn your consent to receive required notices and disclosures electronically from us and you will no longer be able to use the DocuSign system to receive required notices and consents electronically from us or to sign electronically documents from us.

All notices and disclosures will be sent to you electronically

Unless you tell us otherwise in accordance with the procedures described herein, we will provide electronically to you through the DocuSign system all required notices, disclosures, authorizations, acknowledgements, and other documents that are required to be provided or made available to you during the course of our relationship with you. To reduce the chance of you inadvertently not receiving any notice or disclosure, we prefer to provide all of the required notices and disclosures to you by the same method and to the same address that you have given us. Thus, you can receive all the disclosures and notices electronically or in paper format through the paper mail delivery system. If you do not agree with this process, please let us know as described below. Please also see the paragraph immediately above that describes the consequences of your electing not to receive delivery of the notices and disclosures electronically from us.

How to contact Toptal, LLC

You may contact us to let us know of your changes as to how we may contact you electronically, to request paper copies of certain information from us, and to withdraw your prior consent to receive notices and disclosures electronically as follows:

To advise Toptal, LLC of your new e-mail address

To let us know of a change in your e-mail address where we should send notices and disclosures electronically to you, you must send an email message to us at legal@toptal.com and in the body of such request you must state: your previous e-mail address, your new e-mail address. We do not require any other information from you to change your email address..

In addition, you must notify DocuSign, Inc. to arrange for your new email address to be reflected in your DocuSign account by following the process for changing e-mail in the DocuSign system.

To request paper copies from Toptal, LLC

To request delivery from us of paper copies of the notices and disclosures previously provided by us to you electronically, you must send us an e-mail to legal@toptal.com and in the body of such request you must state your e-mail address, full name, US Postal address, and telephone number. We will bill you for any fees at that time, if any.

To withdraw your consent with Toptal, LLC

To inform us that you no longer want to receive future notices and disclosures in electronic format you may:

- i. decline to sign a document from within your DocuSign session, and on the subsequent page, select the check-box indicating you wish to withdraw your consent, or you may;
- ii. send us an e-mail to legal@toptal.com and in the body of such request you must state your e-mail, full name, US Postal Address, and telephone number. We do not need any other information from you to withdraw consent.. The consequences of your withdrawing consent for online documents will be that transactions may take a longer time to process..

Required hardware and software

Operating Systems:	Windows® 2000, Windows® XP, Windows Vista®; Mac OS® X
Browsers:	Final release versions of Internet Explorer® 6.0 or above (Windows only); Mozilla Firefox 2.0 or above (Windows and Mac); Safari™ 3.0 or above (Mac only)
PDF Reader:	Acrobat® or similar software may be required to view and print PDF files
Screen Resolution:	800 x 600 minimum

Enabled Security Settings:	Allow per session cookies
----------------------------	---------------------------

** These minimum requirements are subject to change. If these requirements change, you will be asked to re-accept the disclosure. Pre-release (e.g. beta) versions of operating systems and browsers are not supported.

Acknowledging your access and consent to receive materials electronically

To confirm to us that you can access this information electronically, which will be similar to other electronic notices and disclosures that we will provide to you, please verify that you were able to read this electronic disclosure and that you also were able to print on paper or electronically save this page for your future reference and access or that you were able to e-mail this disclosure and consent to an address where you will be able to print on paper or save it for your future reference and access. Further, if you consent to receiving notices and disclosures exclusively in electronic format on the terms and conditions described above, please let us know by clicking the 'I agree' button below.

By checking the 'I agree' box, I confirm that:

- I can access and read this Electronic CONSENT TO ELECTRONIC RECEIPT OF ELECTRONIC CONSUMER DISCLOSURES document; and
- I can print on paper the disclosure or save or send the disclosure to a place where I can print it, for future reference and access; and
- Until or unless I notify Toptal, LLC as described above, I consent to receive from exclusively through electronic means all notices, disclosures, authorizations, acknowledgements, and other documents that are required to be provided or made available to me by Toptal, LLC during the course of my relationship with you.
